

SITE OBSERVATION REPORT

Project:	Equinix CL1 Mantrap	Project No:	2201319
Location:	Calgary, AB	Report No:	1
Contractor:	Ellis Don	Date of Visit:	2025-09-02
Building Permit No:	BP2024-00799	Report Date:	2025-09-09
		Sheet:	1 OF 4

Reason for Site Visit: Final Review

Present: Tenzin Blair & Ash Parmar

The comments included in this site observation report describe only those items observed at the time of the visit and are not to be construed as a detailed evaluation of the progress of the work or the state of compliance with the Contract Documents. This report does not express any engineering opinion and therefore is not a general review report unless authenticated by the licensed review engineer. It is the responsibility of the contractor(s) to carry out their own inspection of the Work to determine compliance with the Contract Documents.

The correction of any noted deficiencies must be confirmed in writing before a further review will be carried out.

Section A - Progress Summary

1. New luminaires and devices installed adjacent to circle lock and mantrap, respectively:



Figure 1 - New Luminaires Adjacent to Circle Lock

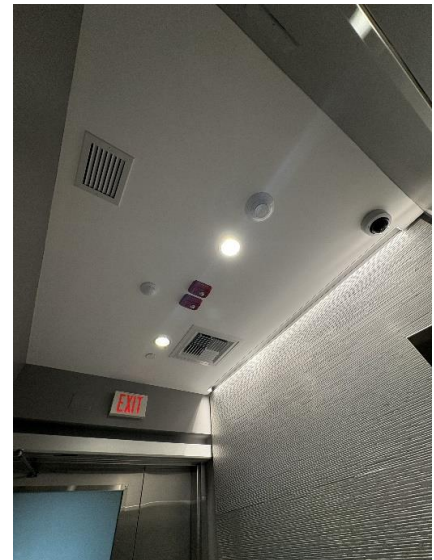


Figure 2 - New Luminaires, FA, Security, and Exit in Mantrap

2. New manual stations installed on secure side and inside of mantrap. Security installation ongoing:

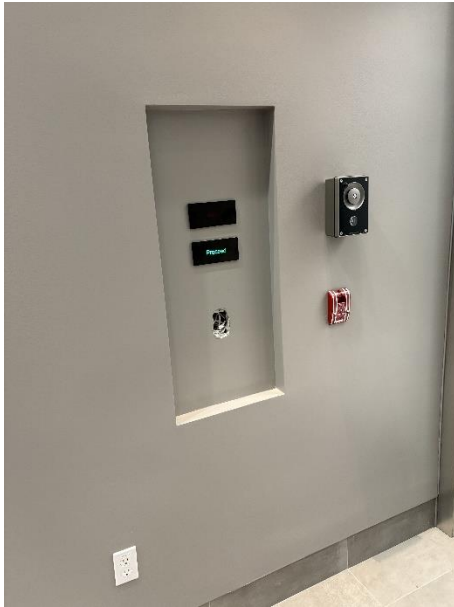


Figure 3 – Manual Station Installed on Secure-Side of Mantrap (Security Installation Ongoing)

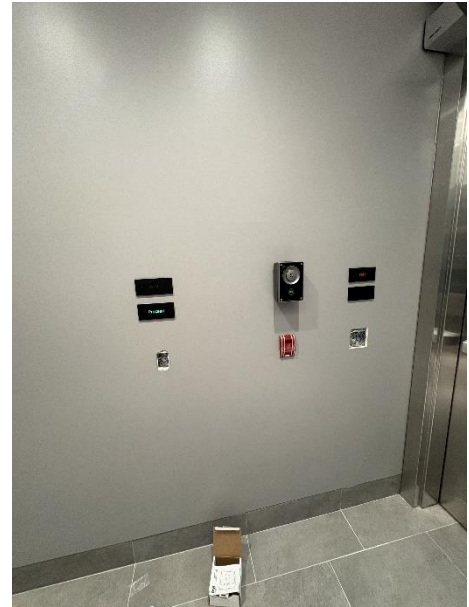


Figure 4 - Manual Station Installed Inside Mantrap (Security Installation Ongoing)

3. New exit signs and horn strobes installed on secure side of mantrap:



Figure 5 - New Secure-Side Horn Strobes & Exit

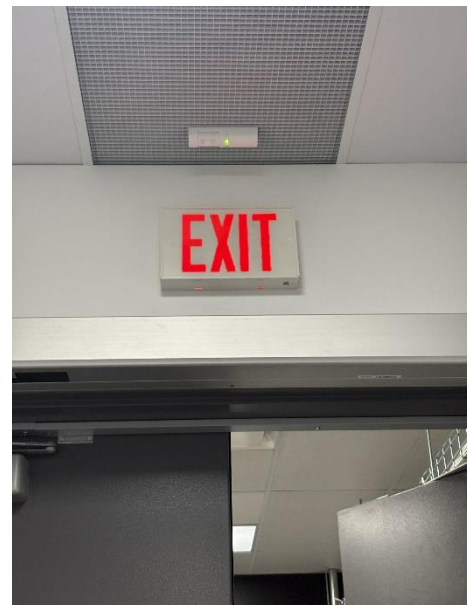


Figure 6 - New Exit Sign at Data Hall Exit

4. Sprinkler Installation on secure side of circle lock and inside data center:

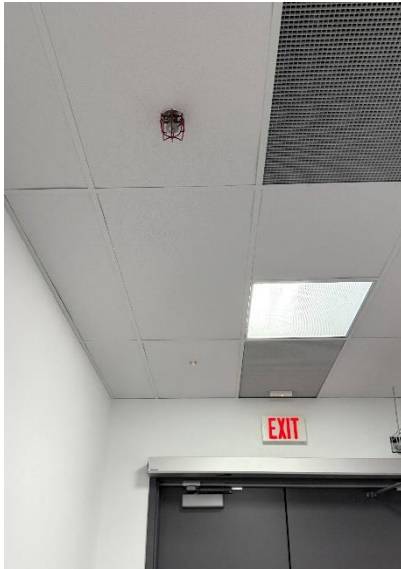


Figure 7 - Sprinkler Data Center Side of Double Door



Figure 8 - Sprinklers at Entrance Side of Double Door

Section B - Deficiencies Note on Completed Work

1. Electrical

- 1.1 During the site observation, it was noted that an existing exit sign scheduled for removal, located at the end of Corridor-1, has been disconnected but not yet demolished (refer to figure below). Electrical contractor shall provide photographic evidence upon completion of associated demolition and patching.

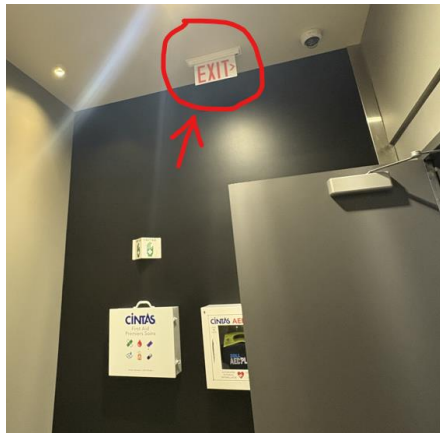


Figure 9 - Exit Sign to be Demolished

- 1.2 During the site observation, it was noted that new fire alarm devices have not been labelled. Electrical contractor shall label all fire alarm devices with typeset adhesive labels.
- 1.3 During the site observation, it was noted that the electrical contractor utilized/extended existing circuits within the space. Electrical contractor shall provide photographic evidence of updated, typeset panel schedules, indicating all existing and revised circuits.

1.4 HHA-E require the following documentation prior to providing an electrical occupancy letter:

- Passing inspection report from Electrical Authority having Jurisdiction.
- Letter from electrical contractor certifying that electric strikes allow for egress on FA alarm and power failure.
- Letter from electrical contractor certifying all emergency lighting is complete and functional.
- Letter from electrical contractor certifying all exit signs are complete and functional.
- FA verification report passed and certified by a licensed engineer.

2. **Mechanical:**

2.1 During the site observation, it was noted that the two sprinkler heads which were issued as part of the revised drawings have not been installed. The issued package, identified as *GC-M-PC-007* dated 2025-06-23, required sprinkler heads to be added on either side of the double doors (Reference sheet F120 – Android L&F Phase 2, Mantraps Replacement, Bankers Hall, 315-8th Avenue S.W., Calgary, AB). These additions were indicated on the drawings; however, they were not observed on site. The Contractor is requested to review and confirm the installation requirements, with a plan for corrective action.

- Drawing reference: Sheet F120
- Issuance reference: Issued for GC-M-PC-007, dated 2025-06-23

2.2 HHA-M have received the Air Balancing Reports, the Sprinkler Verification Letter, and the Schedule C from the Fire Protection Engineer of Record. These documents are currently under review.

Distribution:

H.H. ANGUS AND ASSOCIATES LTD.

- ✓ Project File
- ✓ Owner
- ✓ Prime Consultant
- ✓ GM/CM

Prepared by: Tenzin Blair & Ash Parmar
